



Capital Projects Update


Seth Garcia

Director of Capital Projects

October 21, 2025

ID 25-1593

Overview Of Bonnie Brae Area

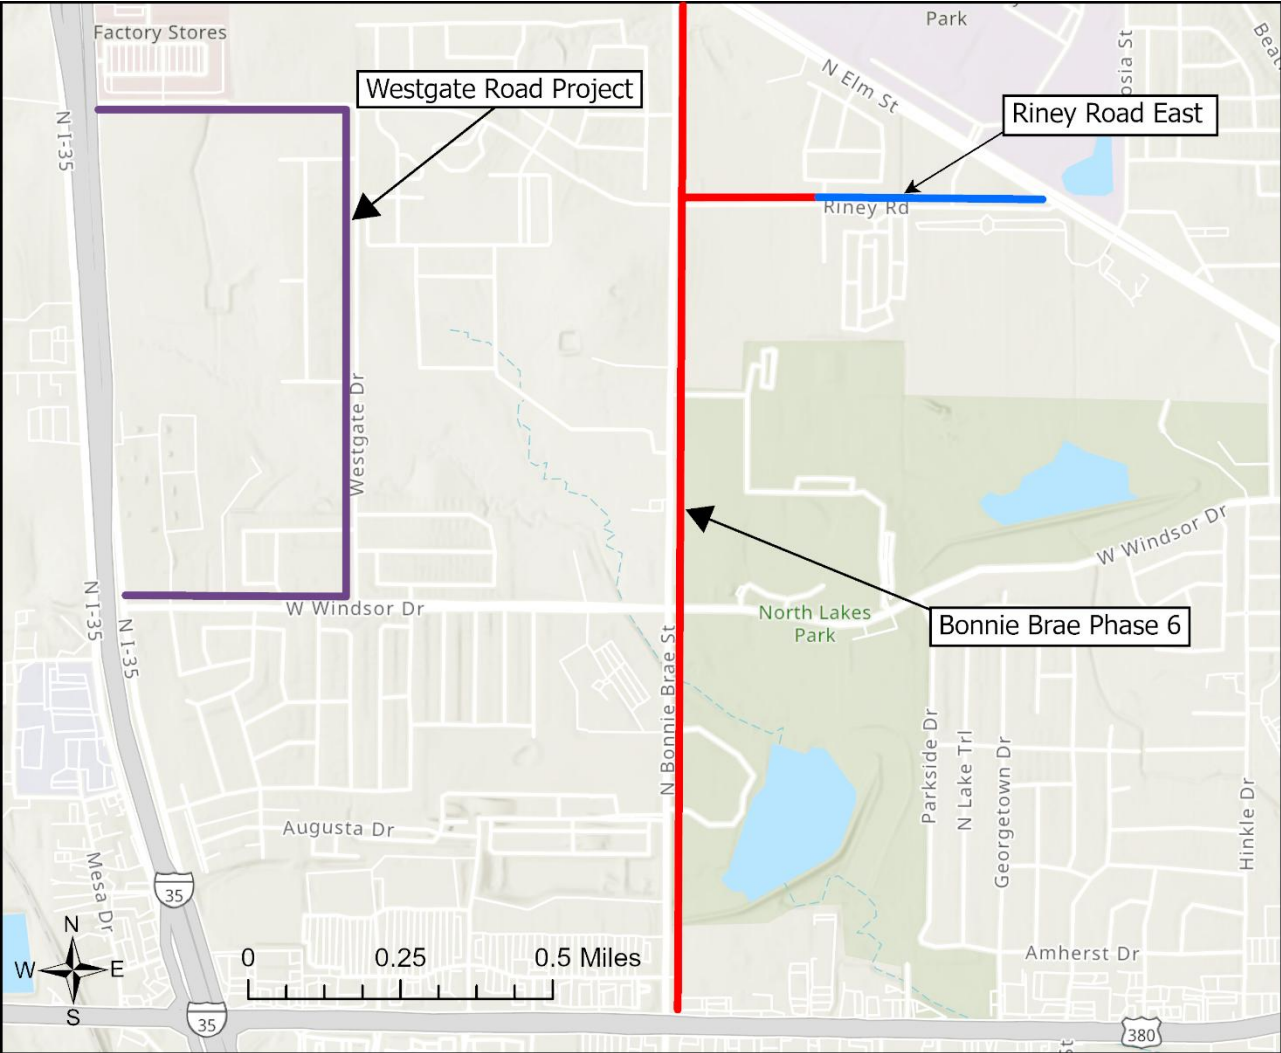

Legend

Bonnie Brae Phase 6

Riney Road East

Westgate Road Project


Bonnie Brae Phase 6 - US 380 to US 77

- Project Scope:
 - Roadway Widening
 - Pedestrian Facilities
 - Utility Installation
 - Traffic Signals and Lighting
- Project Schedule:
 - Current Phase – Construction
 - Construction Start –Q1 2025
 - Construction Complete –Q2 2027
- DISD Coordination:
 - ILA for Improvements to Riney Road - COMPLETED
 - Construction Coordination with Opening of Reeves Elementary
 - Water Service provided in April 2025
 - Traffic Control and Paving complete August 2025



Riney Road East – West of Hardaway Road to US 77

- Project Scope:
 - Roadway Widening
 - Pedestrian Facilities
 - Utility Relocations
 - Park Trails
- Project Schedule:
 - Current Phase – Bid/Award
 - Construction Start – Q1 2026
 - Construction Complete – Q4 2026
- DISD Coordination:
 - Trail System to align with Reeves Elementary School
 - Reviewing traffic crossings to ensure student safety

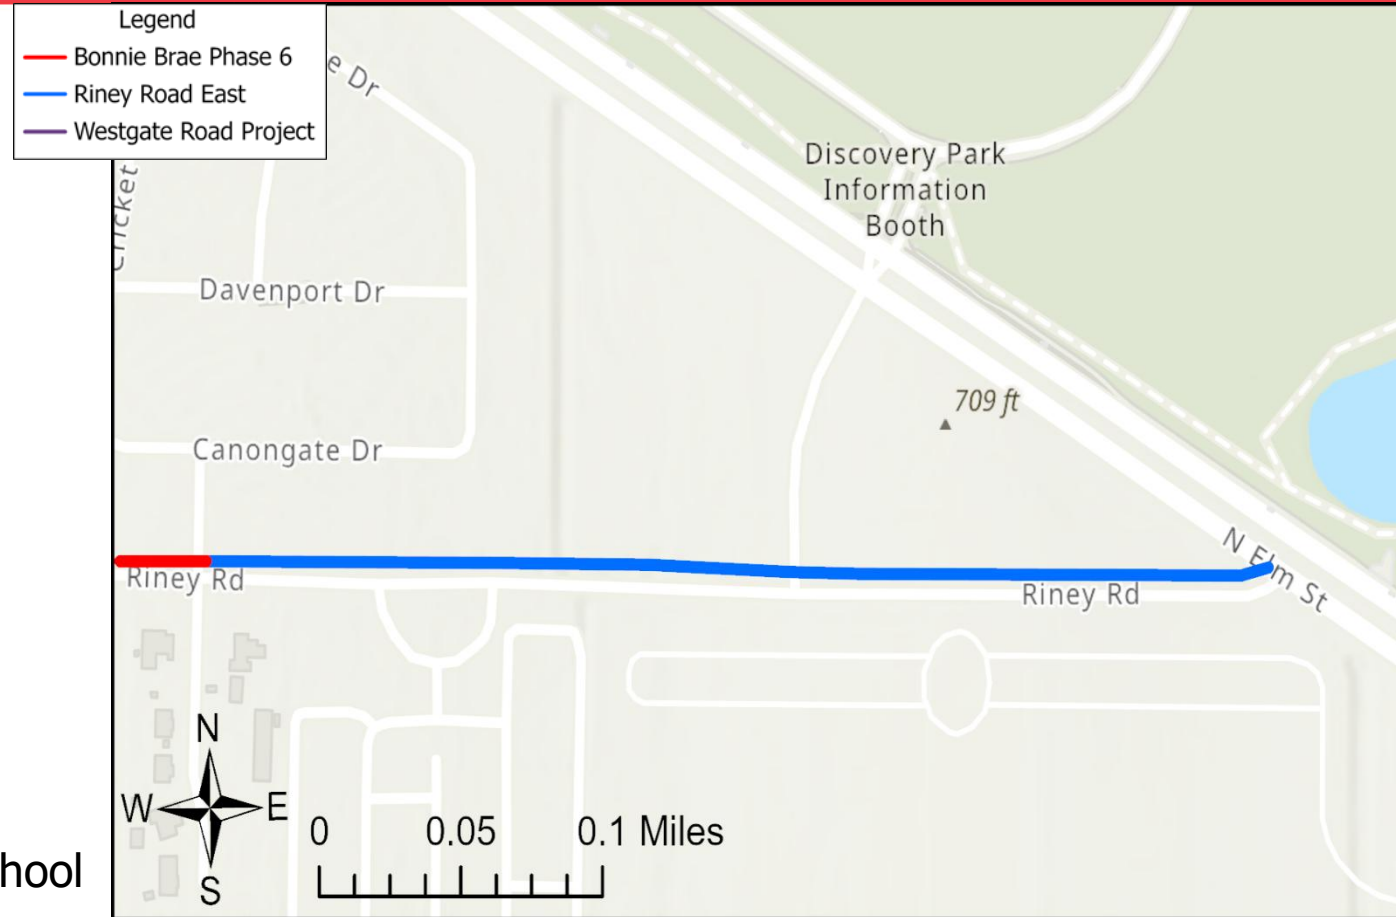


Westgate Road Project including Windsor Drive

- Project Scope:
 - Roadway Widening
 - Pedestrian Facilities
 - Utility Installation
 - Drainage Installation
- Project Status:
 - 90% Design N/S phase
 - Construction – E/W phase
 - Construction Start – Q2 2025
 - Construction Complete – Q4 2027
- DISD Coordination:
 - Connection to Bronco Way in Fall 2025
 - Renaming existing E/W Westgate to Bronco Way when completed





Neighborhood 2 & 6

- Project Scope:
 - Roadway Reconstruction
 - Pedestrian Facilities
 - Utility Replacements
- Project Schedule:
 - Construction Phase – Current
 - Construction Start – Q4 2023
 - Construction Complete – Q4 2026
- DISD Coordination:
 - Impacts to Newton Rayzor Elementary Bus Routes and School Traffic during construction on Cordell and Alice.
 - Communication of street closures/utility work on Congress, Mounts, and Denton street for Old Calhoun Site.

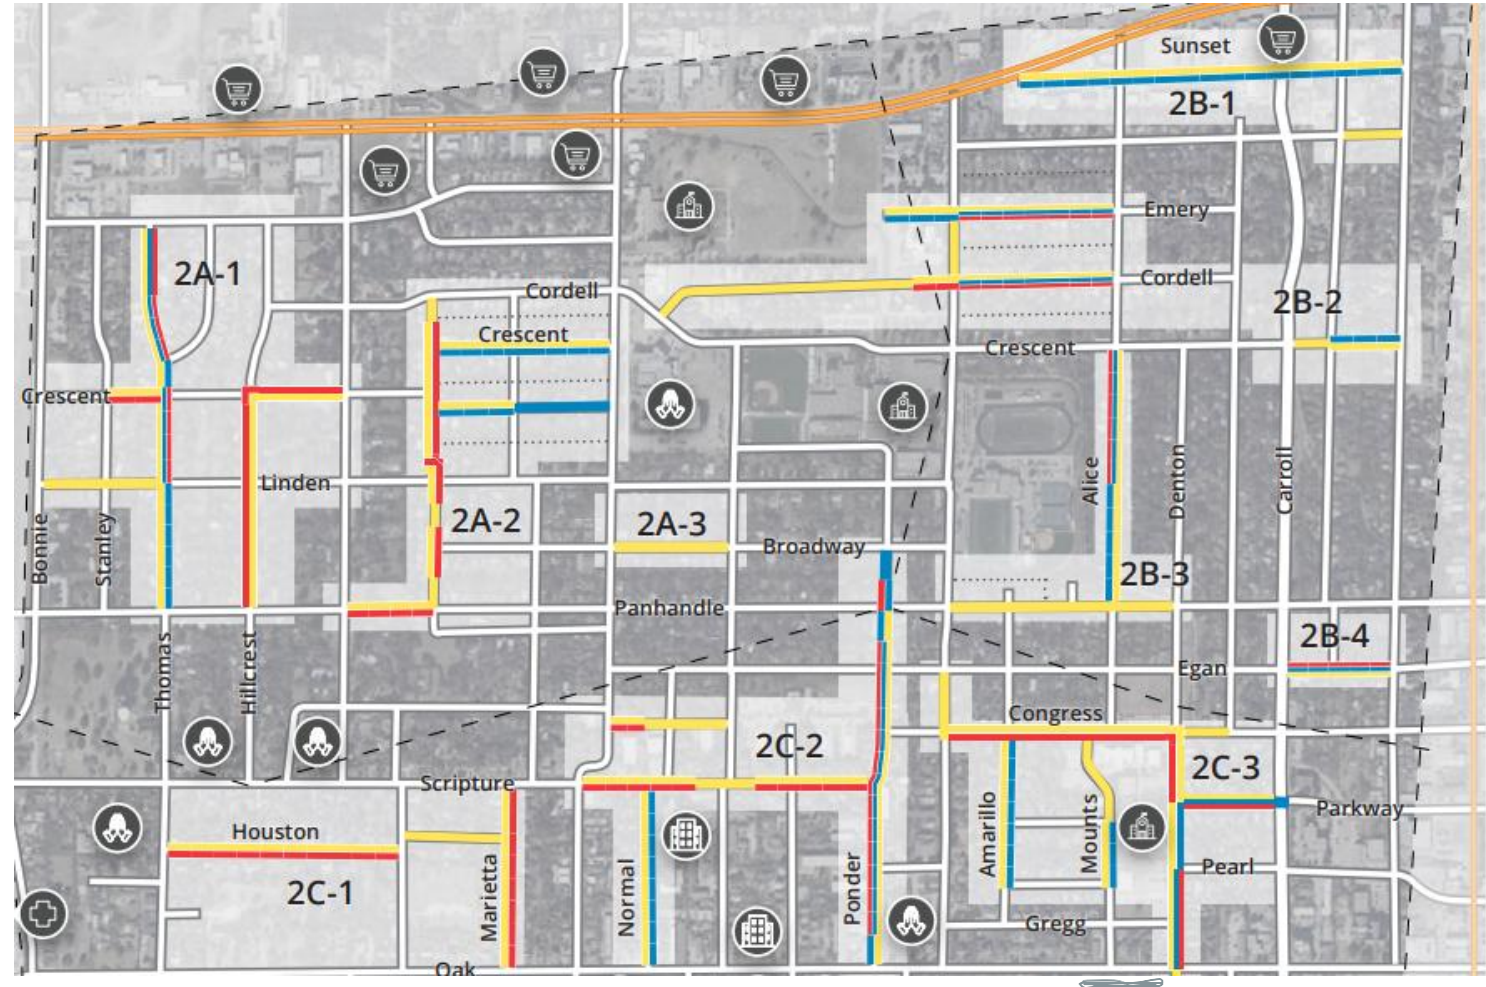

Safe Routes to Schools – Pecan Creek/Nette Shultz

- Project Scope:
 - 5-foot sidewalks near Pecan Creek and Nette Shultz Elementary Schools
- Project Schedule:
 - Current Phase – Construction
 - Construction Start – May 2025
 - Construction Complete – Q4 2026
- DISD Coordination:
 - Working with contractor to prioritize school segments during summer.

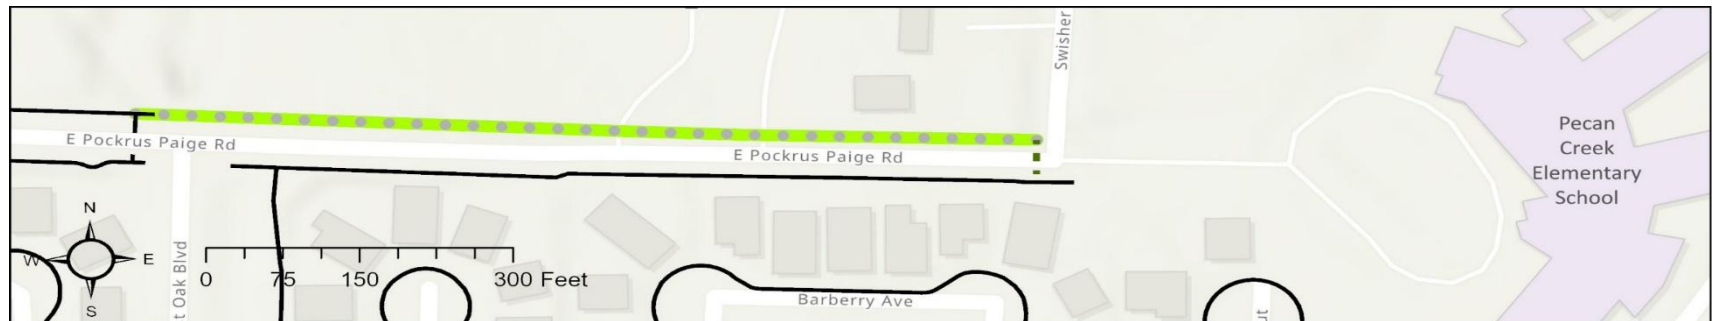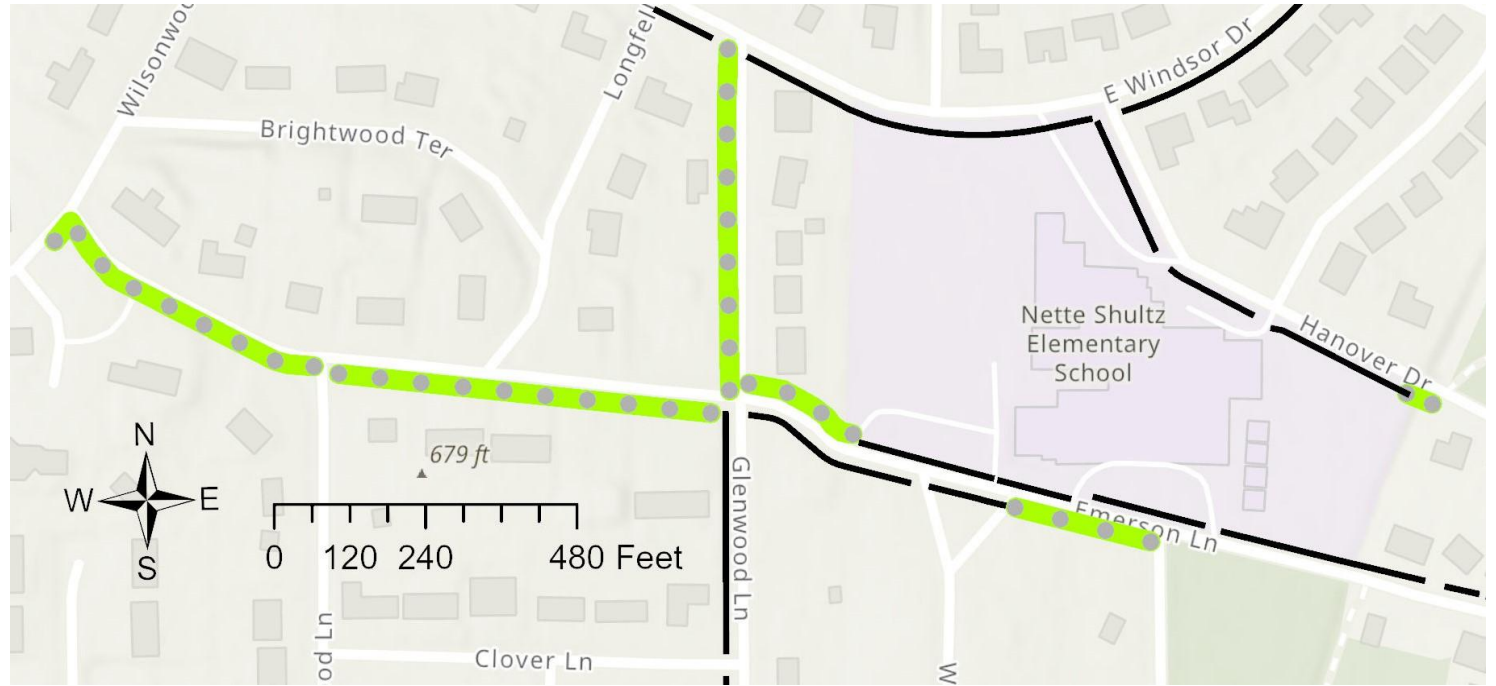

Safe Routes to Schools – Ginnings/Alexander

- Project Scope:
 - 5-foot sidewalks near Ginnings and Alexander Elementary Schools
- Project Schedule:
 - Current Phase – Construction
 - Construction Start – May 2025
 - Construction Complete – Q4 2026
- DISD Coordination:
 - Working with contractor to prioritize school segments during summer.



Questions?

Seth Garcia, PMP

Director of Capital Projects

(940) 349-8938
