

Capital Projects & Engineering

September 5, 2025



IMPROVING DENTON

9/5/25 # BOC25-010

Presentation Overview

- Bond Program Project Updates
 - ➤ Bonnie Brae Road and Hickory Creek Road Overview
 - ≥2014 Bond Proposition 1
 - ≥2019 Bond Proposition 1
 - ≥2019 Bond Neighborhood Rehabilitation Program
 - ➤ 2023 Bond Program Update





BONNIE BRAE ROAD

- **Limits:** US 377 to Loop 288 (8.14 miles)
- **Scope:** Widen from 2 Lanes to 4 lanes including 2 bridge structures, drainage systems, lighting, sidewalks, water, and wastewater improvements, and mixed-use trails.

• Status Update:

- Bonnie Brae Phase 1 Complete
- Bonnie Brae Phase 2 Complete
- Bonnie Brae Phase 3 **Under Construction**. Estimated Completion Q4 2026
- Bonnie Brae Phase 4A Complete, 4B (2014 Bond Program) and 5 (2019 Bond Program) Design Phase
- Bonnie Brae Phase 6 (2019 Bond Program) **Under Construction**. Estimated Completion Q1 2027.

Hickory Creek Road



• Scope: Construct/Widen to a 6-lane divided facility

- Status Update:
 - HC Ph 1 Complete
 - HC Ph 2 Complete.
 - HC Ph 3 Construction resumed May 2025. Bridge work is back underway. Gas line relocation agreements in progress.





Project Name	Scope	Schedule	Budget	2023	2024	2025	2026	2027	2028
Sidewalk Improvements	•	•	•						
Bonnie Brae Phase 4B	•		0						
McKinney/Downtown Quiet Zones	•		0						
Morse Street - 288 to Mayhill	•	0	0						

Bonnie Brae Phase 4B

- Denton County TRIP 2022 Funding Candidate (Approved) Construction funds on hold.
- Project currently on hold

McKinney/Downtown Quiet Zones

- > Schedule dependent on UPRR approval of pedestrian improvements and material availability
- \triangleright Construction to begin once UPRR can acquire material (6 12 month lead time)
- > Estimated Bid Date Q1 2026
- > UPRR estimate for construction increased 1.2M

Morse Street

> Complete!

2014 BOND - Proposition 1

2019 Bond Program



Project Name	Scope	Schedule	Budget	2023	2024	2025	2026	2027	2028
Bonnie Brae Phase 5	•	•							
Bonnie Brae Phase 6	•	•	•						
Hickory Creek Road Phase 3	•	•	0						
Ryan Road Widening	•	0	0						

Bonnie Brae Phase 5

- Denton County TRIP 2022 funding candidate
 (Approved) Funding being reallocated to Elm/Locust
- Project funding was reallocated by Council on December 17.

Bonnie Brae Phase 6

- Project Awarded
- Construction underway. Completion Q1 2027
- > Riney Rd paving complete


Ryan Road

- Project to begin following completion of Hickory Creek Road Phase 3
- Denton County TRIP 2022 funding candidate (Approved)
- Project currently under design
- > ROW acquisition underway.

2019 BOND - Proposition 1

Neighborhood Rehabilitation Program

Project Name	Segments	Project Phase	Substantial Completion		
MCFC	7	Complete	December 2021		
LOFT	7	Complete	December 2021		
SED-A	23	Complete	September 2023		
SED-B	49	Complete	July 2024		
Neighborhood 4	24	Complete	December 2024		
Neighborhood 7A	11	Complete	May 2024		
Neighborhood 1A	22	Complete	May 2024		
Neighborhood 2 and 6	118	Construction	December 2026		
Neighborhood 7B	9	Design	TBD		
Neighborhood 8A	10	Design	TBD		
Neighborhood 8B	5	Design	TBD		
Neighborhood 1B	47	Construction	December 2026		
Neighborhood 5A	48	Design	TBD		

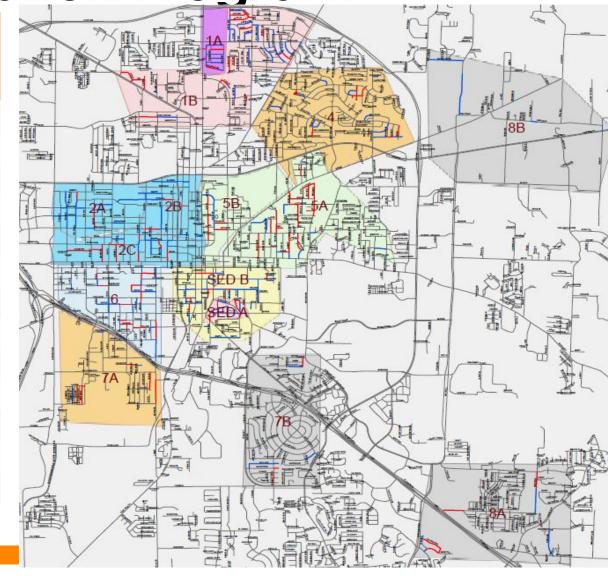



2023 Bond Projects

Project Name	Scope	Schedule	Budget	2023	2024	2025	2026	2027	2028
Pecan Creek Phase 3 & 4	•	•	•						
Oakland Drainage & Upstream Detention	•	•	•						
Mingo/Ruddell/Quiet Zones	•	•	•						
Fire Stations 5 & 6	•	•	•						
Linda McNatt Animal Care & Adoption Center	•	•	•						
Aquatic Improvements	•	0	0						
Active Adult Center	•	•	•						
South Branch Library	•	•	•						

- Fire Stations 5 & 6
 - Under construction
 - ➤ 22.6M GMP approved by Council 7/22/2025
- Oakland Drainage & Upstream Detention
 - Under design
 - ROW/Easement acquisition ongoing
- Ruddell/Mingo/Quiet Zones
 - Under Design
 - Ongoing Railroad coordination

- PEC Phases 3 & 4
 - ROW acquisition in progress
 - Design Plans being brought to 100%
- Linda McNatt Animal Care & Adoption Center
 - Under Design
 - Additional funding approved by Council December 17.
- Aquatic Improvements
 - On hold pending direction from CMO











