
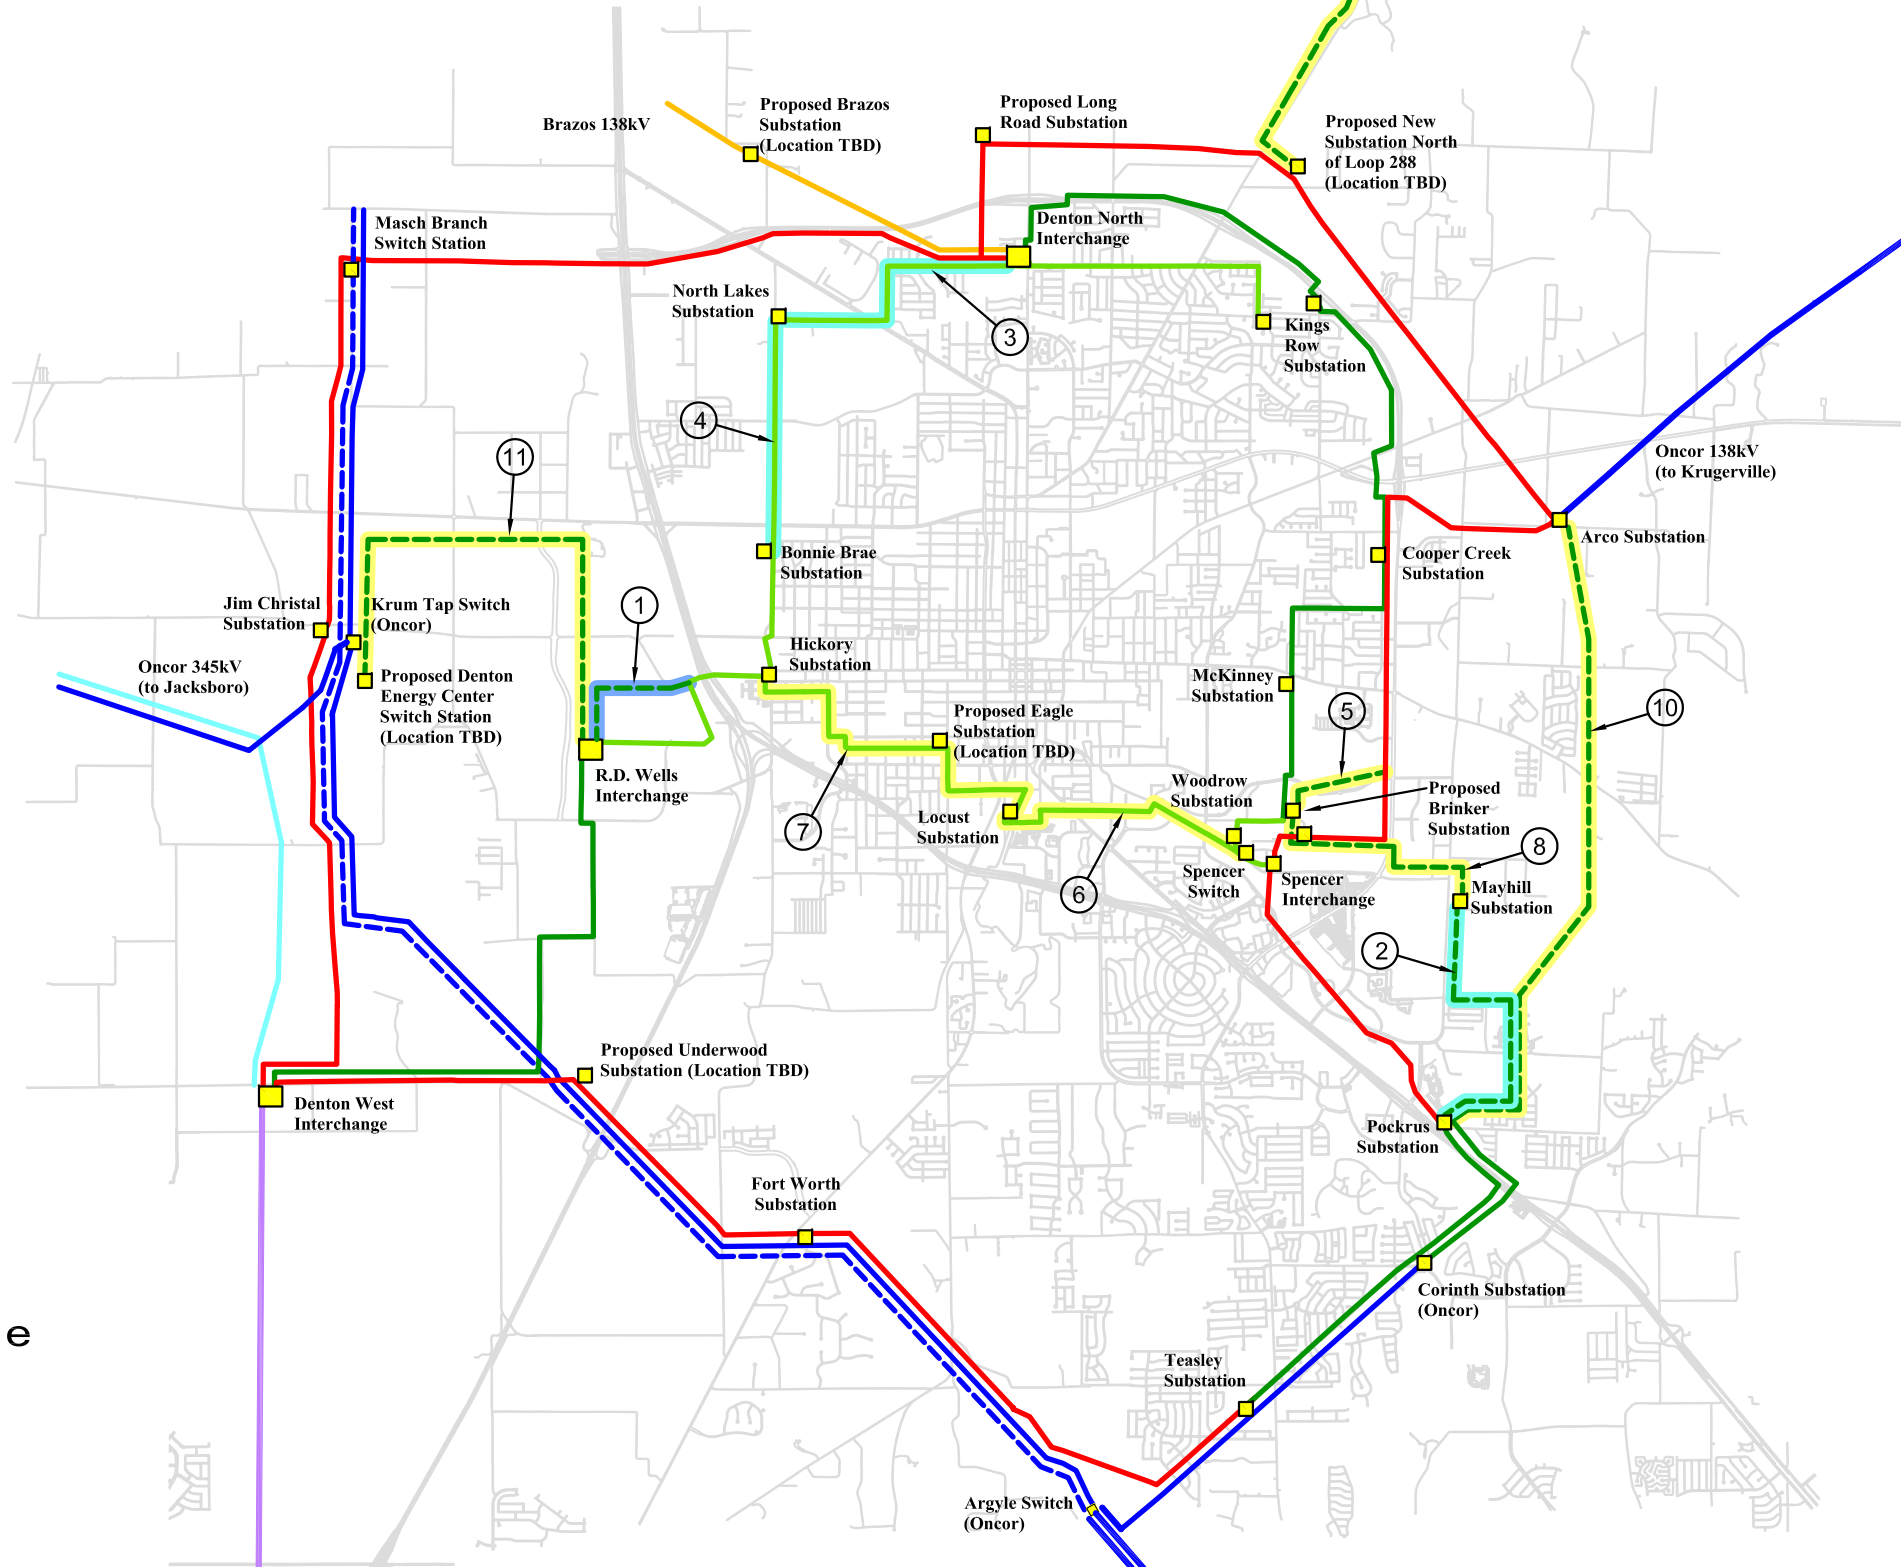


- DME 69KV
- DME 138KV
- ONCOR 138KV
- ONCOR 345KV
- TMPA 138KV
- TMPA 345KV
- BRAZOS 138KV

- ROUTE SELECTION REQUIRED
- ROUTE APPROVED/EASEMENTS REQUIRED
- ROUTE EASEMENTS PROCURED



Denton Municipal Electric Transmission Line Project Status

Route Easements Procured

1. Pacar TM Line Reroute -Projected energize - 2021

Route Approved/Easements Required

2. Pockrus to Mayhill - Projected energize - 2017
3. Denton North to North Lakes TM Line - Projected energize - 2017
4. North Lakes to Bonnie Brae TM Line - Projected enegized 2017. Convert to 138kV - 2019

Route Selection Required

5. Brinker to Loop 288 - Projected energize - 2018
6. Locust to Spencer TM Line - Projected energize 2018
7. Hickory to Locust TM Line - Projected energize - 2019
8. Mayhill to Brinker - Projected energize - 2020
9. Green Valley Energy Center - Northside TM Line - Pojected energize - 2020
10. Pockrus to Arco - Projected energize - 2021
11. Denton Energy Center to RD Wells - Projected energize 2021.

Completed Projects

- Spencer - Pockrus (TMPA) - Completed April 2015
- Teasley - Pockrus - Completed May 2015
- McKinney - Cooper Creek - Completed June 2015
- Woodrow - McKinney - Completed Oct. 2015
- Cooper Creek - Kings Row - Completed Dec. 2015
- Kings Row - Denton North - Completed Dec. 2015
